



FACILITIES

BOND CONSTRUCTION PROJECTS

103

Total construction projects - Phases 1-4

19

Complete

38

Under construction

46

In planning/design

25


In Phase 5

UNDER CONSTRUCTION

- Agricultural Science Center
- Anderson Elementary
- Blanton Elementary
- Boles Junior High
- Career and Technical Center
- Crow Elementary
- Duff Elementary
- Ellis Elementary
- Foster Elementary
- Little Elementary
- Martin High School
- Miller Elementary
- Pearcy Elementary
- Remyse Elementary
- Sam Houston High School
- Sherrod Elementary
- Turning Point Secondary School

[SEE ALL](#)

CAMPUS PROJECTS STATUS*

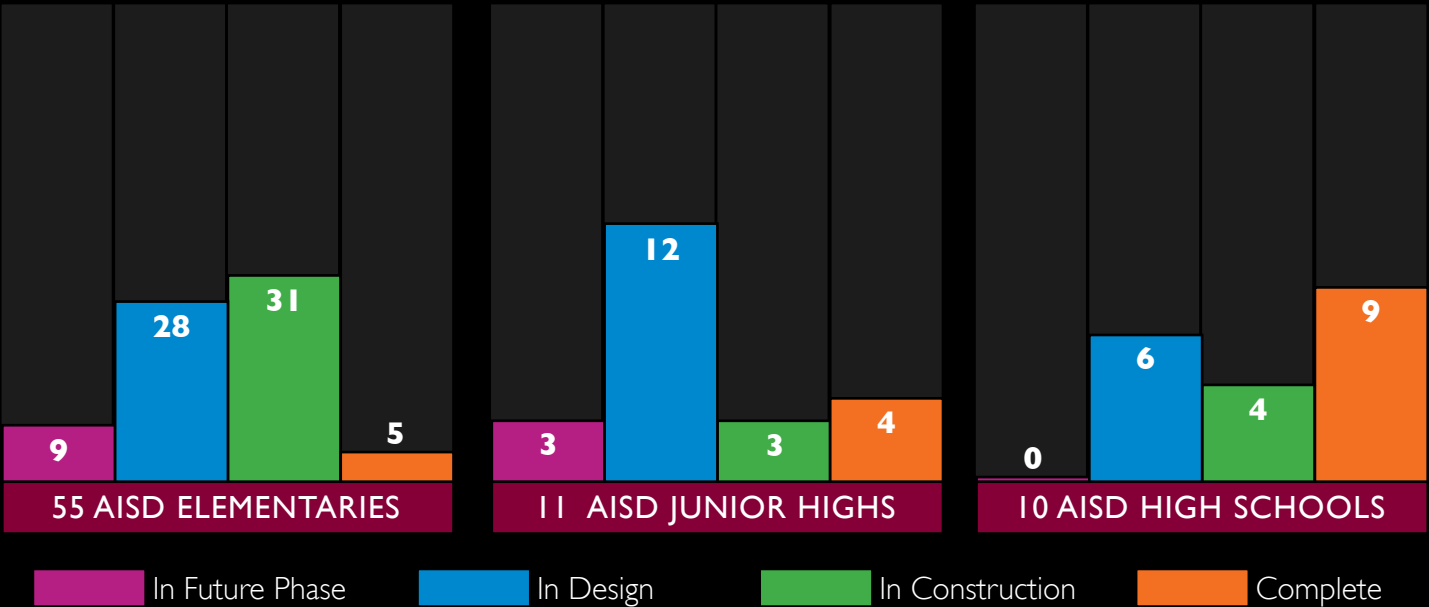


The number of projects is greater than the number of schools as some schools have multiple projects designed and executed at different times.


BY BOND PHASE

PHASE 1-4 PROJECTS

- Phase 1
- Phase 2
- Phase 3
- Phase 4

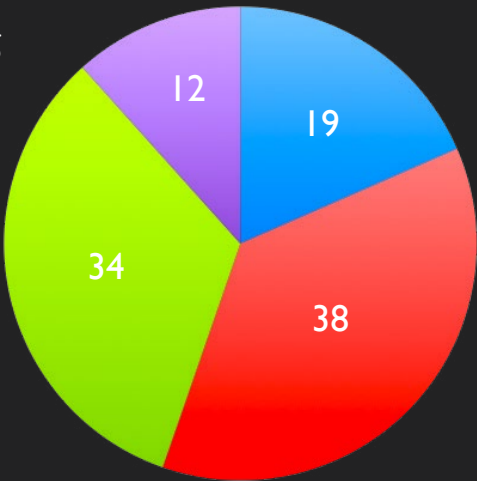

CONSTRUCTION BOND BUDGET

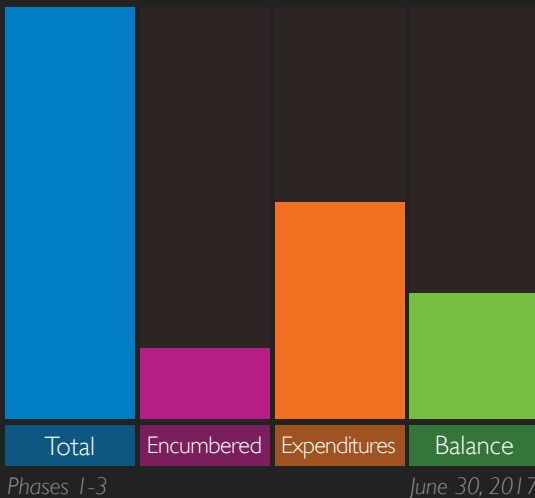



SECURITY/TECHNOLOGY

CLASSROOM TECHNOLOGY STANDARDS

A/V

AUDIO/VISUAL
49/73 schools complete

T

TEACHER
72/73 schools complete

S

STUDENT
73/73 schools complete
with Chromebooks

L


ELEMENTARY LIBRARY
53/53 schools complete

DISTRICT BANDWIDTH




INCREASED 200%
SINCE THE BOND

NETWORK/WIRELESS UPGRADES AT EACH SCHOOL

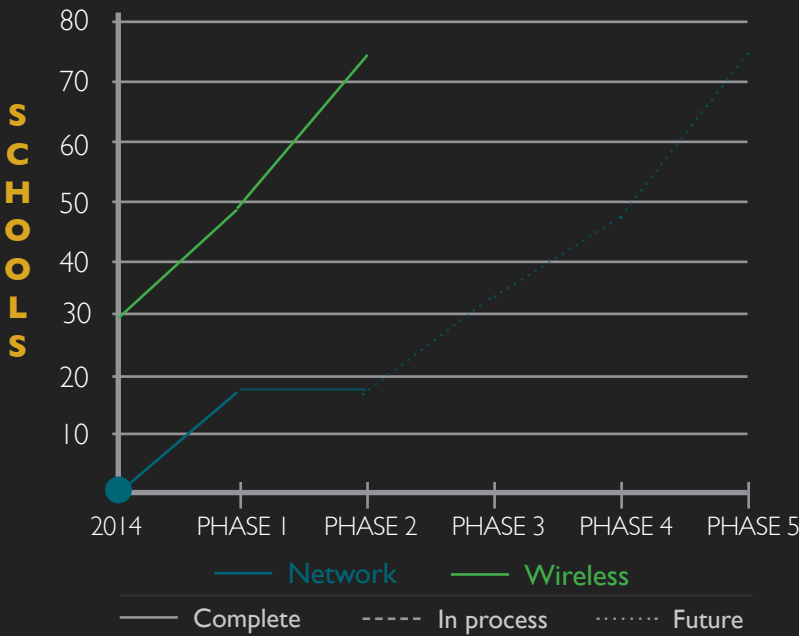


SECURITY/TECH BOND BUDGET



Phases 1-3


June 30, 2017

NEW SECURITY CAMERAS AT EACH SCHOOL

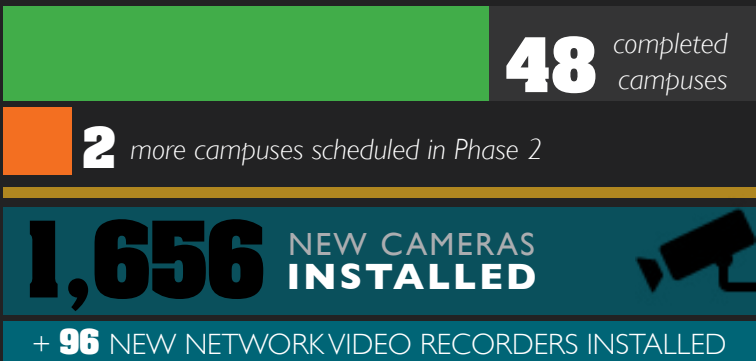

FINE ARTS

NEW INSTRUMENTS



PHASE 1: 1,325

PHASE 2: 1,386

PHASE 3:

PHASE 4:

PHASE 5:

TOTAL: 2,711

NEW UNIFORMS

NEW UNIFORMS FOR BAND, CHOIR,
ORCHESTRA AND DRILL TEAM



210

2,325

Phase 1


Phase 2

Phase 3

Phase 4

Phase 5


FINE ARTS BOND BUDGET

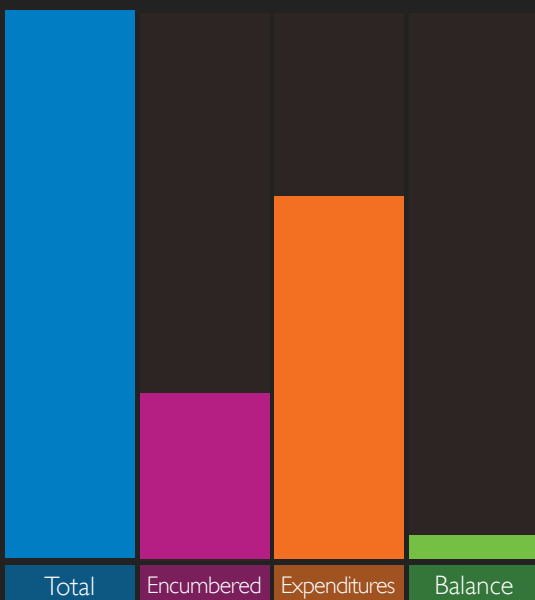

Phases 1-3

June 30, 2017

INSTRUMENTAL MUSIC PARTICIPATION

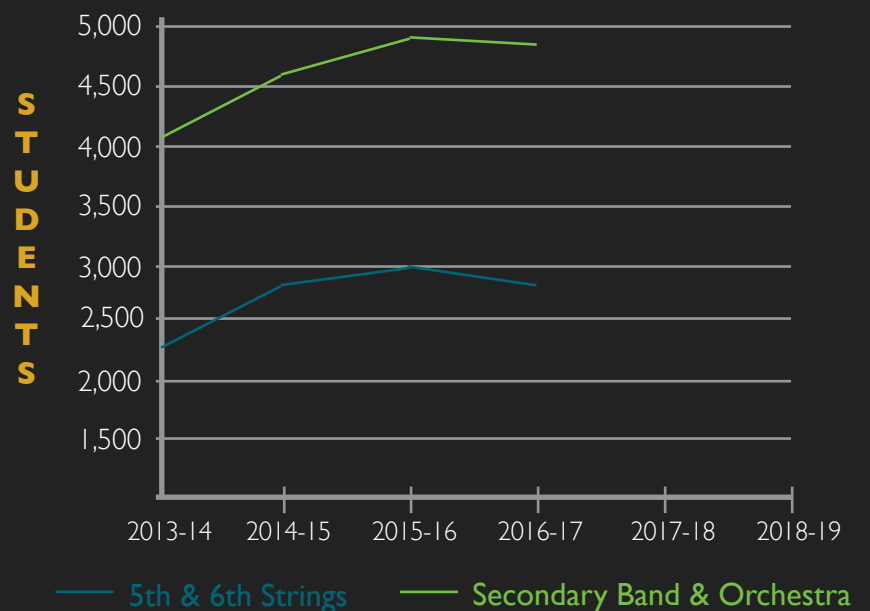

TRANSPORTATION

SCHOOL BUSES



72

ordered and delivered

- 51 regular ed buses
- 21 special ed buses

114

total new buses in the five-year bond program

NEW SCHOOL BUSES

WHITE FLEET

150

total new service vehicles in the five-year bond program

96

ordered and delivered

NEW SERVICE VEHICLES



ZONAR



IMPLEMENTATION PROCESS


**INSTALL
ON BUSES**

COMPLETE

**ROLL OUT
TO STUDENTS**

IN PROCESS

TRANSPORTATION BOND BUDGET

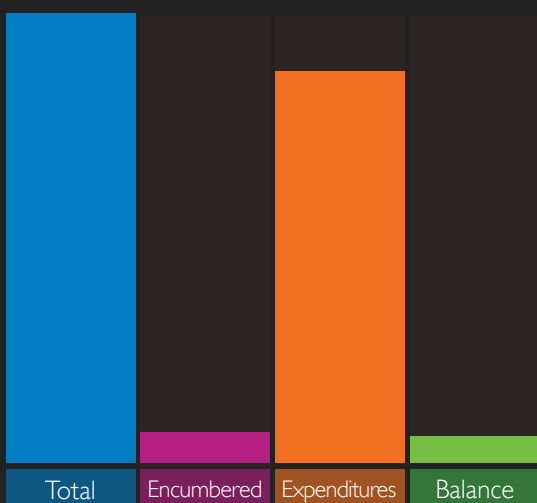

Phases 1-3

June 30, 2017

AISD BUS FLEET

