

2019 BOND UPDATE REPORT AND BOND PLANNING DISCUSSION

June 17, 2025



Bond Program Financial Summary (Phases I-V)

	Budget	Encumbered	Expended	Available	Remaining
Facilities	\$852,726,335	\$108,713,740	\$508,894,184	\$235,118,411	\$0
Fine Arts	\$6,955,752	\$116,067	\$5,187,746	\$1,651,939	\$0
Technology	\$90,829,000	\$3,224,960	\$72,099,605	\$15,504,435	\$0
Transportation	\$15,488,913	<u>\$1,573,481</u>	\$7,720,566	\$6,194,866	<u>\$0</u>
Totals	\$966,000,000	\$113,628,248	\$593,902,101	\$258,469,650	\$0
			Bond Issuance Costs	-\$5,242,704	
			Projected Interest Arbitrage Liability	-\$20,977,755	
			Interest and Additional		
			Proceeds Total Available	<u>\$52,625,842</u>	
			Funds	\$284,875,033	

Note: Totals may not add due to rounding. Information as of May 1, 2025.





Active Projects – by Phase

(Bond Phases I – V)

Phase	Number of Projects
Planning	12
Design	24
Bid	3
Construction	25
Closeout	3
Completed	32
Total Projects	99

Facilities – Joey Rodriguez Junior High School



Facilities – Glaspie Field Construction







HUB Participation

PHASES I-V


Project Description	Budget	Tier II HUB Participation Commitment %	Tier II HUB Participation Amount	Expenses To Date	Tier II % HUB Participation Achieved To Date	Tier II HUB Participation Amount To Date
2019 BOND PROGRAM PHASES I-V HUB TOTALS	\$ 556,189,154	23.45%	\$ 130,398,981	\$ 437,480,558	24.66%	\$ 107,895,800

Note: Totals above are excerpted from the 06/01/2025 HUB report



Facilities – Schematic Site Drawing - Glaspie Field

GLASPIE FIELD - CURRENT DESIGN

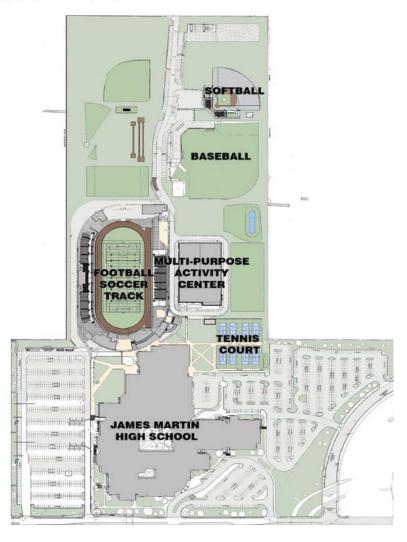






Facilities - Cravens Field

CRAVENS FIELD - EXISTING CONDITION

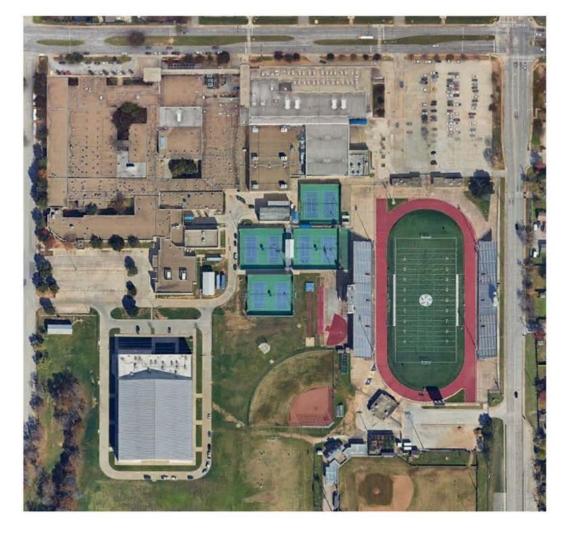






Facilities - Cravens Field

CRAVENS FIELD - EXISTING WITH GLASPIE OVERLAY

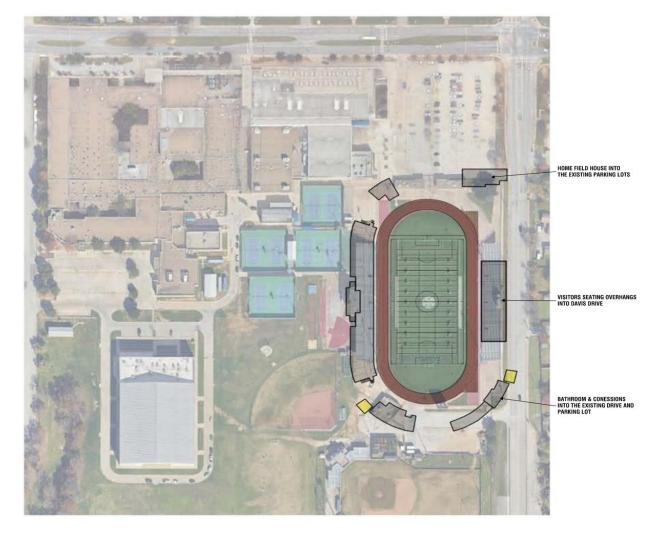






Facilities – Schematic Site Drawing - Cravens Field

CRAVENS FIELD - CURRENT DESIGN

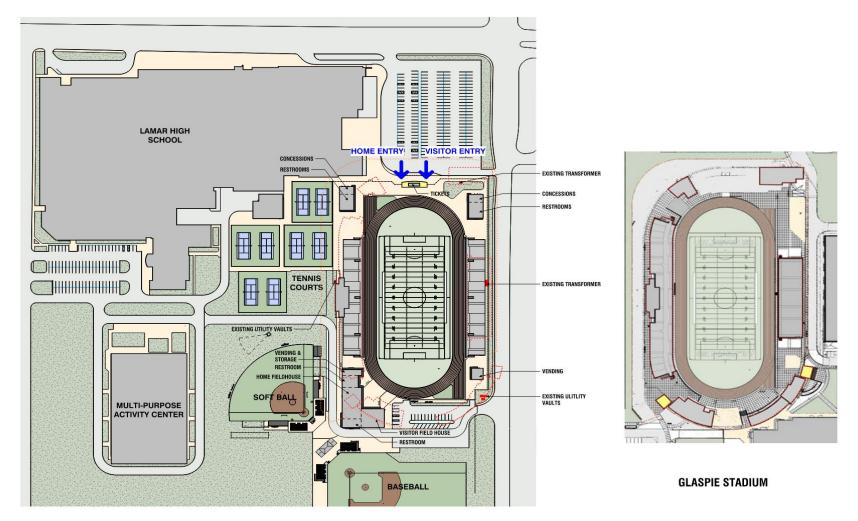






Facilities – Revised Schematic Site Drawing - Cravens Field

CRAVENS FIELD - REVISED PLAN

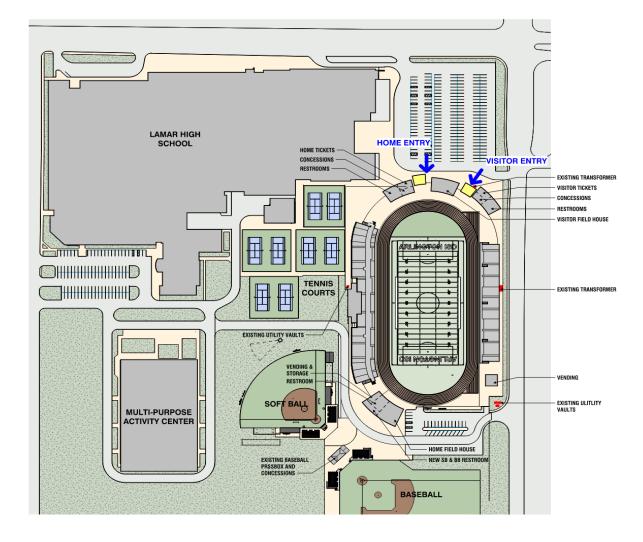





Facilities - Wilemon Field

WILEMON FIELD - EXISTING CONDITION







Facilities - Wilemon Field

WILEMON FIELD - EXISTING WITH GLASPIE OVERLAY








Facilities – Schematic Site Drawing – Wilemon Field

WILEMON FIELD - CURRENT DESIGN

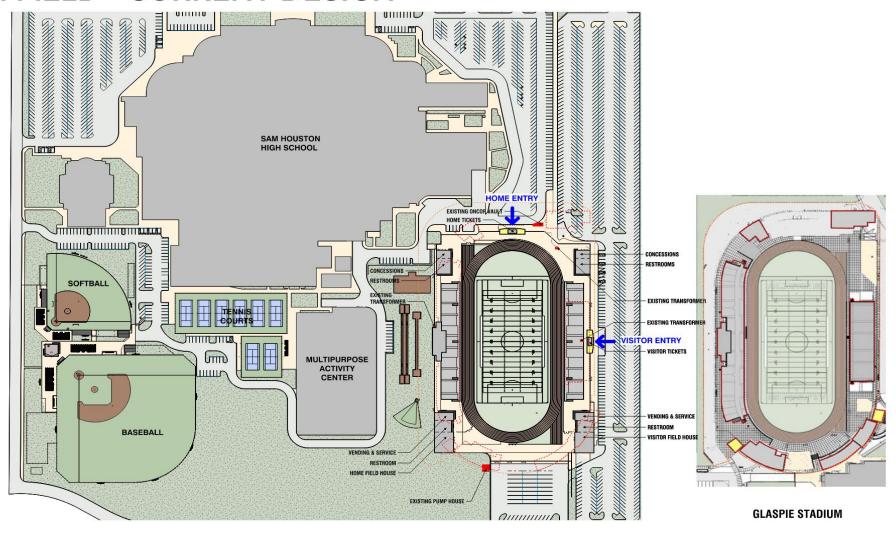






Facilities – Revised Schematic Site Drawing - Wilemon Field

WILEMON FIELD - REVISED PLAN

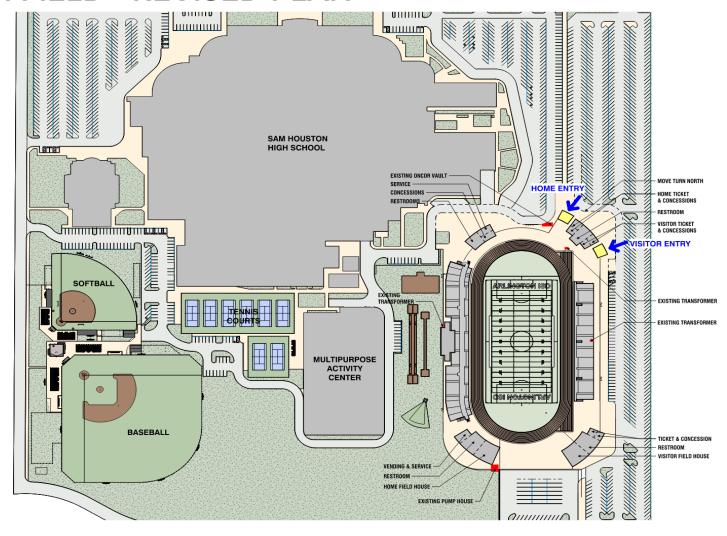





Facilities – Schematic Rendering – Wilemon Field Entry



Facilities – Schematic Rendering – Wilemon Field Aerial View





Facilities – Schematic Rendiering - Cravens Field Entry





Facilities – Schematic Rendering - Cravens Field Aerial View





Facilities

Glaspie, Cravens & Wilemon Field Comparison

Area	Glaspie	Cravens	Wilemon
Press box (SF)	8,144	8,144	8,144
Home Locker Room (SF)	2,760	2,760	2,760
Visitor Locker Room (SF)	2631*	2,760	2,760
Vending / Concessions	1,900	1,900	1,900
Storage:	800	800	800
Total Area:	24,121	24,250	24,250
Fixture Count			
Male Toilets/Urinals	46	46	46
Male Sinks	17	17	17
Femail Toilets	58	58	58
Femail Sinks	22	22	22
Unisex Toilets	4	4	4
Unisex Sinks	4	4	4
Drinking Fountains	14	14	14

The Glaspie Field locker rooms are rectangular in snape creating a minor difference. This is negated by the design efficiency.

